

SAN JOSE SHELTER FOR THE HOMELESS

COST FREE CLARIFICATION

Maxim Schrogin
Oliver and Co.,
1035 Carleton Street,
Berkeley 94710.

CLARIFICATION no: 57
Date: 5/1/89

REGARDING DINING HALL ROOF SHEATHING

This clarification is issued in accordance division 1, section 1.7 of the contract specifications, for the purpose of clarifying the drawings and/or specifications. This clarification shall in no event result in an increased cost.

Sheathing for the dining hall roof will be 1 1/8" AC tongue and groove plywood. Plywood shall be installed with the A face down. The face grain of the plywood will run parallel with the 4X6 purlins. All plywood joints will fall on purlins or blocking at trusses. Nailing shall be according to schedule on original drawings (Sheet D-3).

4X4 BLOCKING shall be installed at roof peak according to the attached sketch.


SIGNATURE

R. P. Schrogin
For CES

For Oliver and Company



SEP 9 1989

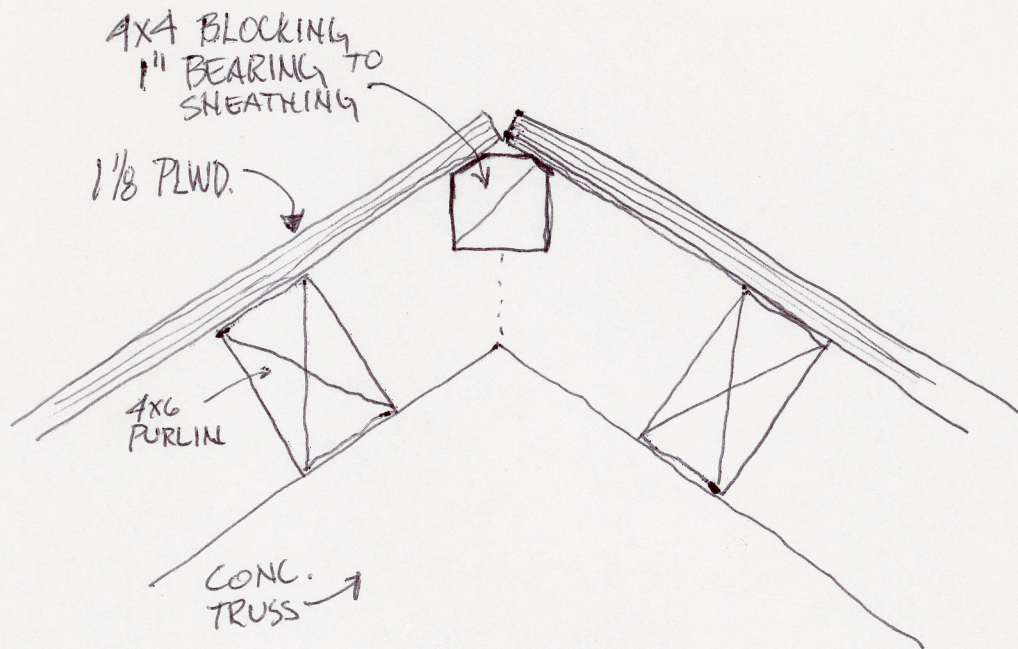

4x4 BLOCKING AT
ROOF PEAK

CLARIFICATION 57

5/1/89

J.M.



sup Q. 2.30.89
